



## Construction

### PROJECT TITLE

In-Line Baggage System - CIP No. 0113

### PROJECT DESCRIPTION

This project provides construction services for a new In-Line Baggage Handling System located at the south end of the commercial terminal building. The design includes new expanded baggage screening and make-up areas and utilizes the current version of the TSA guidelines and standards.

### STATUS OF PROJECT


Notice to Proceed was issued on January 29, 2024. The contractor set up a temporary fence and removed the canopy in front of the Snack Shack. Complete demolition of the Snack Shack is anticipated to be complete in the next couple of weeks.

### PROJECT FUNDING

Description	Estimated Cost	TSA	PFC	FDOT
Design	\$825,303	95%	5%	
Construction	\$20,852,925	\$12M	\$4.2M	\$3.2M

### PROJECT SCHEDULE

Milestone Description	Completion Date	Completed
TA Accept Scope of Work	Mar-21	✓
TSA Review	Jun/Jul-21	✓
TSA Grant Offer	07/29/21	✓
CCAA Accept Grant and Approve Consultant Agreement	08/19/21	✓
Issue Notice to Proceed	09/03/21	✓
Pre-Design Phase	12/21	✓
Schematic Design Phase	02/22	✓
Detailed Design Phase (Includes 30%, 70%, 100% submittals)	12/22	✓
Advertise for Bids	03/06/23	✓
Bid Opening	04/19/23	✓
Submit Grant Applications	Jun/23	✓
PTGA Grant Offer	8/4/2023	✓
OTA - Construction Grant Offer	8/17/2023	✓
Construction Limited NTP	Sept-2023	✓
Construction Start	Jan-2024	✓
Substantial Completion	Aug-2025	

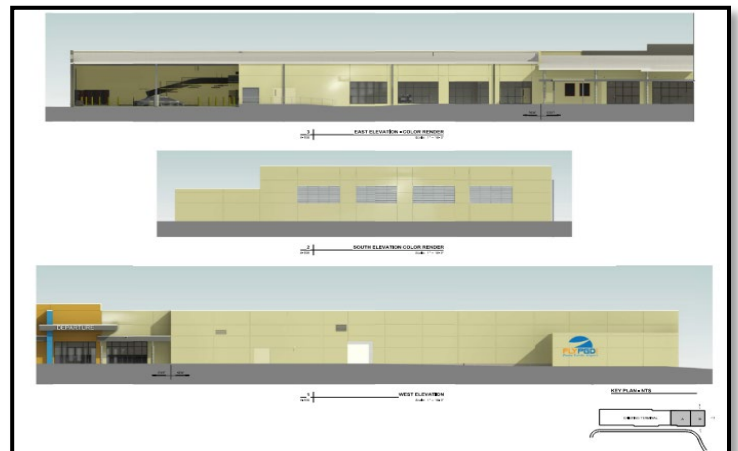

### CONTRACTS

Firm Name	Fee
AECOM - Design	\$825,303
A2 - Construction	\$20,852,925
